



CERTIFICATE OF EXAMINATION

ROR 08

Complete

Score	55 / 56 (98.21%)	Flagged items	0	Actions	0
-------	------------------	---------------	---	---------	---

Site conducted

CA003 Molyneaux Avenue, CALA Homes

Conducted on

11 Mar 2025 9:39 AM UTC

Prepared by

Andy G

Location

(51.7223369, -0.5403753)

Asset

ROR 08
Roller - Hamm 120 Roller - 12VV

Asset serial number

Wgh0h230chaa02109

Asset hours

775

Supply multiple photo's of asset - all sides, any damage etc




Photo 1




Photo 2




Photo 3



Photo 4



Photo 5

Power unit	11 / 11 (100%)
Oil level	Acceptable
Water/Antifreeze level	Acceptable
Belt tension/Condition	Acceptable
Mountings	Acceptable
Emissions/Exhaust	Acceptable
Oil leaks	Acceptable
Hoses & pipes	Acceptable
Gauges/Warning indicators	Acceptable
Turbo	N/A
Air cleaner/Indicator	Acceptable
Spark Arrestor	N/A

Transmission	5 / 5 (100%)
Oil levels/Leaks	Acceptable
Controls/Operations	Acceptable
Drive shafts/Axles	Acceptable
Hub reduction units/levels	Acceptable
Transfer box/levels	Acceptable

Brakes	5 / 5 (100%)
Air/Hydraulic leaks	Acceptable
Drums/Discs/Pads/Shoes	N/A
Foot/Hand controls	Acceptable
Cables/Rods/Pipes	Acceptable
Fluid levels/Efficiency	Acceptable

Steering		6 / 6 (100%)
Box/Column/Wheel		Acceptable
King Pins/Bushes		Acceptable
Ramp/Pump/Hoses		Acceptable
Track Rods/Steering Arms		Acceptable
Linkages/Ball joints		Acceptable
Oil levels/Leakes		Acceptable

Running Gear		4 / 5 (80%)
Tyres/Wheels/Tracks		Acceptable
Wheel bearings		Acceptable
Axle security		Acceptable
Over run brake rods/cable		
Towing/Frame Attachments		Acceptable

Fuel System	4 / 4 (100%)
Fuel tank/Security	Acceptable
Fuel line/leaks	Acceptable
Filters/Pumps	Acceptable
Fuel level/Gauge	Acceptable


Hydraulics		5 / 5 (100%)
Rams		Acceptable
Pumps/Hoses/Pipes		Acceptable
Safety indicators		Acceptable
Oil levels/leaks		Acceptable
Controls		Acceptable

Electrical	10 / 10 (100%)
Battery	Acceptable
Alternator/Charging	Acceptable
Wiring	Acceptable
Fuses/Circuit breakers	Acceptable
Lights/Indicators	Acceptable
Warning Indicators	Acceptable
Outlet sockets	N/A
Limit/Proximity switches	N/A
Safety Devices	Acceptable
Warning Devices	Acceptable

Cab	5 / 5 (100%)
Seating/Belts	Acceptable
Structure/Rops	Acceptable
Glass/Mirrors	N/A
Mountings	Acceptable
Safe access to components, struts and hinges all in working order	Yes

Sign off

Engineers name & signature



11 Mar 2025 9:44 AM UTC

Media summary

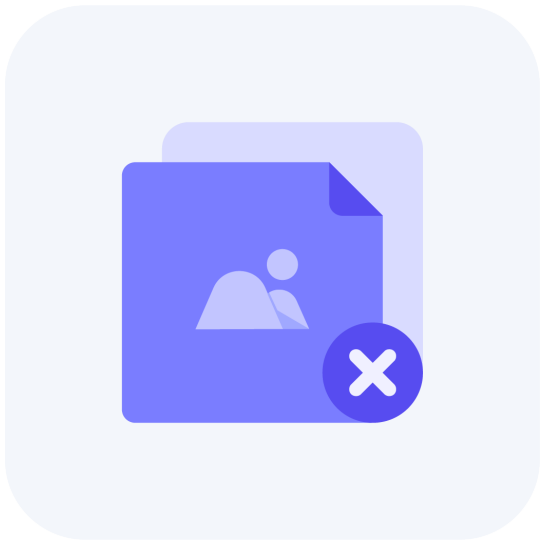


Photo 1

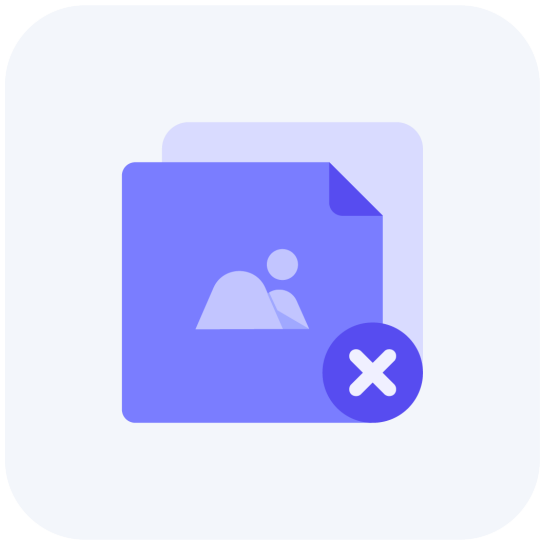


Photo 2

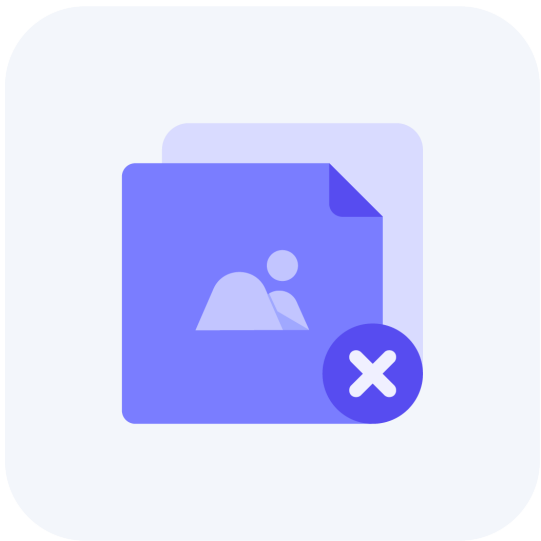


Photo 3



Photo 4



Photo 5
