



2.CERTIFICATE OF EXAMINATION

ASH 950

Complete

Score	56 / 56 (100%)	Flagged items	0	Actions	0
-------	----------------	---------------	---	---------	---

Site conducted

DAN002 Wildacre Rd, Shenley
Wood, Dandara

Conducted on

28 Oct 2025 11:42 AM GMT

Prepared by

Andrew Gibbins

Location

1 Bowmont Drive, Shenley Church
End, Milton Keynes MK5 6GS, UK
(52.0175394, -0.7908014)

Asset

ASH 950
9 Ton Dumper - Dumper 9T
Thwaites MACH 2290

Asset serial number

SLCM22902416G5465

Asset hours

300

Supply multiple photo's of asset - all sides, any damage etc




Photo 1




Photo 2




Photo 3




Photo 4

Power unit	11 / 11 (100%)
Oil level	Acceptable
Water/Antifreeze level	Acceptable
Belt tension/Condition	Acceptable
Mountings	Acceptable
Emissions/Exhaust	Acceptable
Oil leaks	Acceptable
Hoses & pipes	Acceptable
Gauges/Warning indicators	Acceptable
Turbo	Acceptable
Air cleaner/Indicator	Acceptable
Spark Arrestor	N/A

Transmission	5 / 5 (100%)
Oil levels/Leaks	Acceptable
Controls/Operations	Acceptable
Drive shafts/Axles	Acceptable
Hub reduction units/levels	Acceptable
Transfer box/levels	Acceptable

Brakes	5 / 5 (100%)
Air/Hydraulic leaks	Acceptable
Drums/Discs/Pads/Shoes	Acceptable
Foot/Hand controls	Acceptable
Cables/Rods/Pipes	Acceptable
Fluid levels/Efficiency	Acceptable

Steering		6 / 6 (100%)
Box/Column/Wheel		Acceptable
King Pins/Bushes		Acceptable
Ramp/Pump/Hoses		Acceptable
Track Rods/Steering Arms		Acceptable
Linkages/Ball joints		Acceptable
Oil levels/Leakes		Acceptable

Running Gear	5 / 5 (100%)
Tyres/Wheels/Tracks	Acceptable
Wheel bearings	Acceptable
Axle security	Acceptable
Over run brake rods/cable	N/A
Towing/Frame Attachments	Acceptable

Fuel System		4 / 4 (100%)
Fuel tank/Security		Acceptable
Fuel line/leaks		Acceptable
Filters/Pumps		Acceptable
Fuel level/Gauge		Acceptable


Hydraulics		5 / 5 (100%)
Rams		Acceptable
Pumps/Hoses/Pipes		Acceptable
Safety indicators		Acceptable
Oil levels/leaks		Acceptable
Controls		Acceptable

Electrical	10 / 10 (100%)
Battery	Acceptable
Alternator/Charging	Acceptable
Wiring	Acceptable
Fuses/Circuit breakers	Acceptable
Lights/Indicators	Acceptable
Warning Indicators	Acceptable
Outlet sockets	N/A
Limit/Proximity switches	N/A
Safety Devices	Acceptable
Warning Devices	Acceptable

Cab	5 / 5 (100%)
Seating/Belts	Acceptable
Structure/Rops	Acceptable
Glass/Mirrors	Acceptable
Mountings	Acceptable
Safe access to components, struts and hinges all in working order	Yes

Sign off

Engineers name & signature



28 Oct 2025 11:47 AM GMT

Media summary

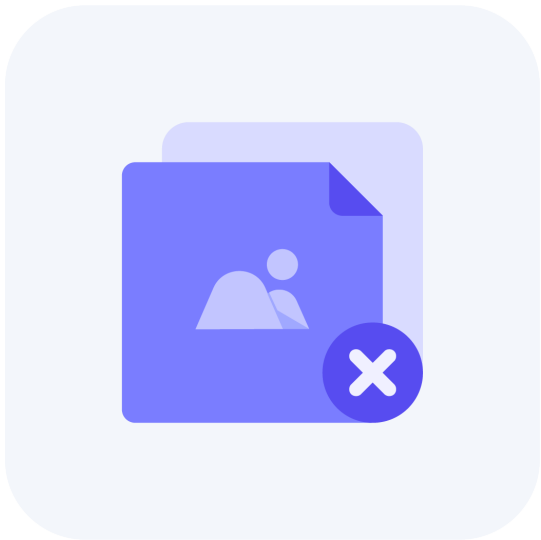


Photo 1

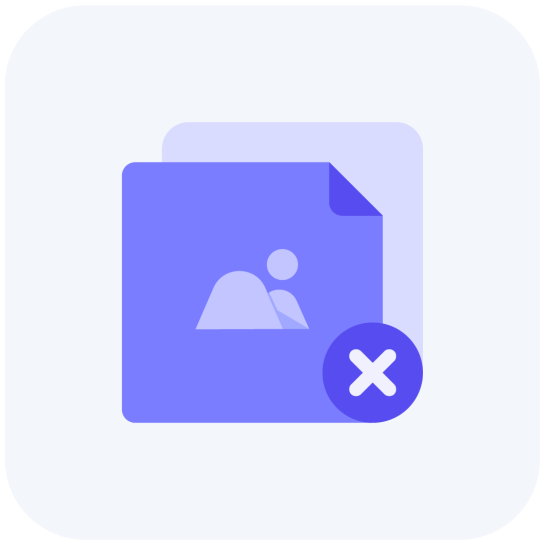


Photo 2

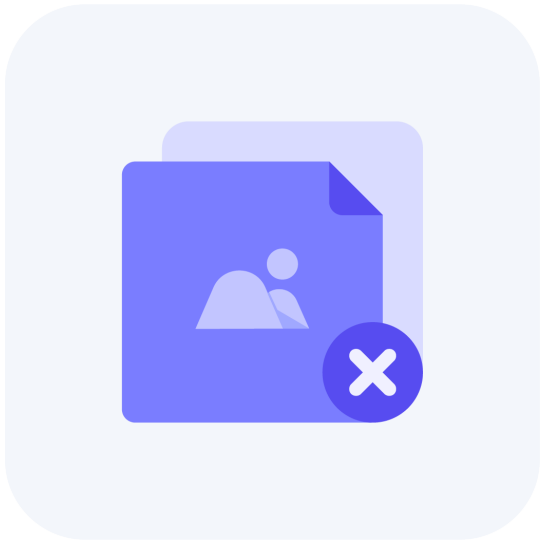


Photo 3

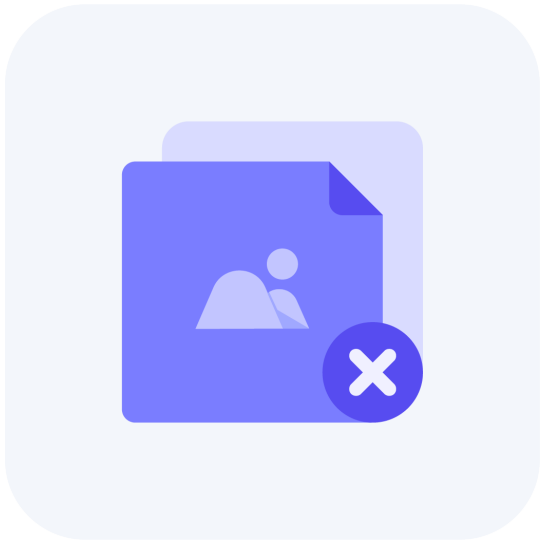


Photo 4
